# Pre-installation agreement Hamwells HomeSpa

EN / V1.1 2020




Pelgrimsstraat 3, 3029 BH, Rotterdam the Netherlands T +31 85 303 6496 E info@hamwells.com I www.hamwells.com



Before your HomeSpa is installed, make sure that your bathroom meets these pre-installation requirements.

# Wall model (reservoir) Unit mm Wall model (reservoir) Unit mm Wall Wall model (reservoir) Unit mm Wall The connections are in the right place The connections are in the right place

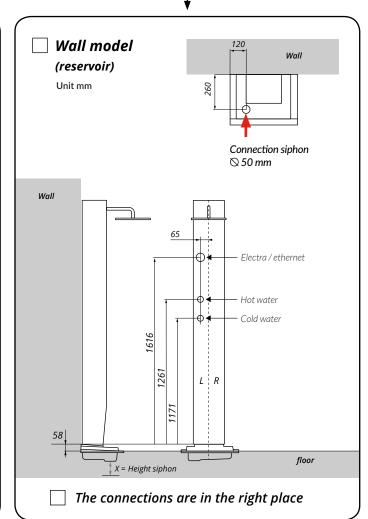

### Does your bathroom meet the 7 points below?

ᆜ	The power supply connection is in the right place, is at least 5A insulated, grounded and has a grounding circuit breaker.
	Your hot and cold water connections are in the right place and are provided with a 1/2 "external connection.
	Your hot water supply is at least 55°C, maximum 3 bar and can provide at least 0.5 liter / min.
	The Ethernet connection is provided with a RJ45 plug and placed in the power supply connection.
	Your drain has a siphon for a 50 mm connection, is in the right place and runs flat with the underfloor.
	Your bathroom is at least 230 cm high and is easily accessible to our installer.
	The bathroom should be completely finished, including tiling.
our ba	throom meets the above points, your Hamwells installer can install your new HomeSpa!
appro	oval,

Signature

# Pre-installation agreement Hamwells HomeSpa

EN / V1.1 2020




Pelgrimsstraat 3, 3029 BH, Rotterdam the Netherlands T +31 85 303 6496 E info@hamwells.com I www.hamwells.com



Place

Before your HomeSpa is installed, make sure that your bathroom meets these pre-installation requirements.

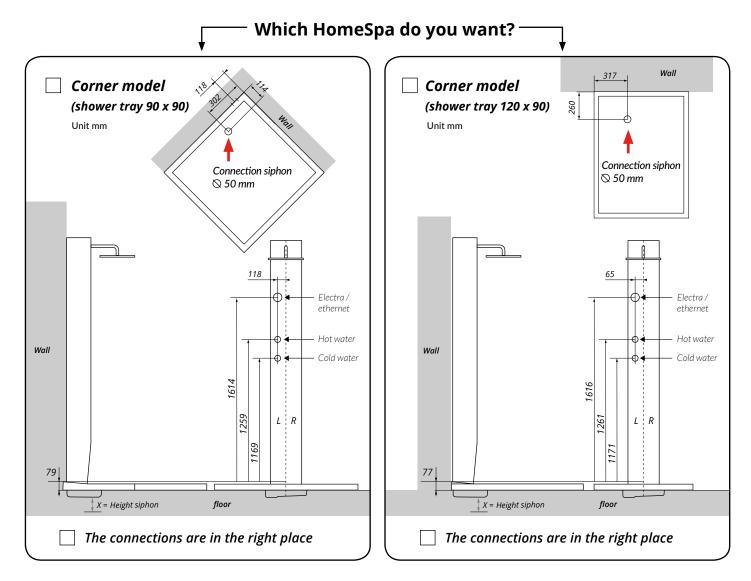

### Does your bathroom meet the 7 points below?

	The power supply connection is in the right place, is at least 5A insulated, grounded and has a grounding circuit breaker. Your hot and cold water connections are in the right place and are provided with a 1/2 "external connection.
	Your hot water supply is at least 55°C, maximum 3 bar and can provide at least 0.5 liter / min.
	The Ethernet connection is provided with a RJ45 plug and placed in the power supply connection.
	Your drain has a siphon for a 50 mm connection, is in the right place and runs flat with the underfloor.
	Your bathroom is at least 230 cm high and is easily accessible to our installer.
	The bathroom should be completely finished, including tiling.
f your bo	athroom meets the above points, your Hamwells installer can install your new HomeSpa! oval,

Name

Signature

# **Pre-installation agreement Hamwells HomeSpa**

EN / V1.1 2020




Pelgrimsstraat 3, 3029 BH, Rotterdam the Netherlands T +31 85 303 6496 E info@hamwells.com I www.hamwells.com



Before your HomeSpa is installed, make sure that your bathroom meets these pre-installation requirements.

## Which HomeSpa do you want? Wall model 255 (reservoir) Unit mm Connection siphon **⊘** 50 mm 330 65 Electra / Wall Cold water L ightharpoonup R1261 58 floor ☐ The connections are in the right place

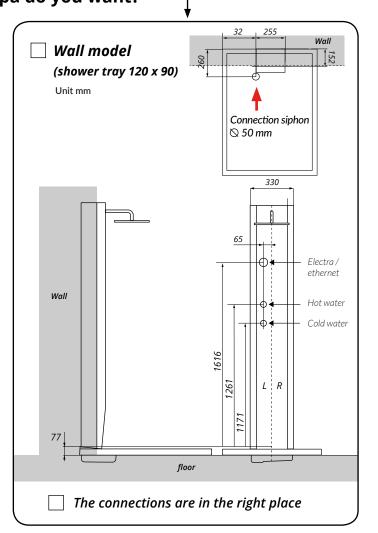

### Does your bathroom meet the 7 points below?

	The power supply connection is in the right place, is at least 5A insulated, grounded and has a grounding circuit breaker.
Ä	Your hot and cold water connections are in the right place, is at least 3A insulated, glounded with a 1/2 "external connection.
	Your hot water supply is at least 55°C, maximum 3 bar and can provide at least 0.5 liter / min.
	The Ethernet connection is provided with a RJ45 plug and placed in the power supply connection.
	Your drain has a siphon for a 50 mm connection, is in the right place and runs flat with the underfloor.
	Your bathroom is at least 230 cm high and is easily accessible to our installer.
	The bathroom should be completely finished, including tiling.
h	
your bo or appr	athroom meets the above points, your Hamwells installer can install your new HomeSpa!

Signature
